

Social Safeguards Monitoring Report

PUBLIC

Semiannual Report (July–December 2025)
January 2026

Kyrgyz Republic: Naryn Rural Water Supply and Sanitation Development Program

Prepared by the Community Development and Investment Agency of the Kyrgyz Republic (ARIS) for the Kyrgyz Republic and the Asian Development Bank (ADB).

CURRENCY EQUIVALENTS

(as of 1 January 2026)

Currency Unit	–	som (Som)
Som1.00	=	\$0.011
\$1.00	=	Som87.25

ABBREVIATIONS

ADB	–	Asian Development Bank
AO	–	Aiyl Okmotu
ARIS	–	Agentstvo Razvitya i Investirovanya Soobshestv (Community Development and Investment Agency)
BFM	–	beneficiary feedback mechanism
DED	–	detailed design and cost estimation documentation
GRM	–	grievance redress mechanism
m	–	meter
mm	–	millimeter
RBL	–	results-based lending
DDWSS	–	Department of “Drinking Water Supply and Sewerage Development” under the Ministry of Water Resources, Agriculture and Processing Industry of the Kyrgyz Republic
WSS	–	water supply and sanitation

NOTE

In this report, "\$" refers to United States dollars.

This social safeguards monitoring report is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or Staff, and may be preliminary in nature. Your attention is directed to the [“terms of use”](#) section of ADB's website.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, ADB does not intend to make any judgments as to the legal or other status of any territory or area

Contents

1	INTRODUCTION	2
1.1	Preamble	2
2	PROGRAM DESCRIPTION AND CURRENT ACTIVITIES	3
2.1	Program Description.....	3
2.2	Program Contacts and Management.....	6
2.3	The Program Activities During the Current Reporting Period.....	13
2.4	Description of Any Changes in the Program Design	18
2.5	Description of Any Changes to Agreed Construction Methods.....	18
3	SOCIAL SAFEGUARDS ACTIVITIES	19
3.1	General Description of Social Safeguards Activities.....	19
3.2	Audit of the Sites	19
3.3	Tracking the Issues (based on Non-Conformance Notifications).....	21
3.4	Tendencies.....	22
3.5	Unforeseen Social Impacts or Risks.....	22
4	GRIEVANCE REDRESS MECHANISM AND BENEFICIARY FEEDBACK MECHANISM.....	23
4.1	GRM.....	23
4.2	BFM.....	24
	ANNEXES.....	26
	Annex 1. Photos from the Construction Sites	26
	Annex 2. List of key documents on Program's Social Safeguards as of 31 December 2025	33

List of Tables

Table 1	Amount disbursed under the Program	2
Table 2	List of villages of Additional Financing of the Program	5
Table 3	Responsibility of Partner Organizations in the Program Implementation	6
Table 4	Program Contracts	8
Table 5	Contact Details of Local Self-Government Bodies covered by the Program.....	9
Table 6	Information on the Program Subprojects under the First Contract for DED Packages (KYRGYZGIPROSTROY OJSC Design Institute)	10
Table 7	Information on the Program Subprojects under the Second Contract for DED Packages (ENKON LLC Design Institute)	11
Table 8	Information on the Program Subprojects under the Third Contract for DED Packages (Consortium: ENKON LLC and KYRGYZGIPROSTROY OJSC)	12
Table 9	Brief Information on Construction Work Contracts and Status.....	15
Table 10	Site Visits and Audits	19

1 INTRODUCTION

1.1 Preamble

1. This report represents the semiannual social safeguards monitoring report for the Naryn Rural Water Supply and Sanitation Development Program (Program).
2. The objective of the Program is inclusive and reliable access to safe water supply and improved sanitation for rural communities in Naryn Region.
3. During the second half of 2025, more than \$ 13 mln. were disbursed under the Program (see Table 1).

Table 1: Amount disbursed under the Program

	Program (Credit # 3854-KGZ (COL); Grant # 0676-KGZ (SF)) – Original Financing (\$)	Program (Credit # 4494-KGZ (COL); Grant # 0971-KGZ (SF)) – Additional Financing (\$)	Total (\$)
Credit	1,860,294.13	1,337,500.00	3,197,794.13
Grant	1,953,583.49	6,750,000.00	8,703,583.49
Government of the Kyrgyz Republic	1,046,109.28	114,942.53	1,161,051.81
Grand total	4,859,986.90	8,202,442.53	13,062,429.43

4. As for the social safeguards, the Program is classified as Category B in accordance with ADB's Safeguard Policy Statement (2009) requirements. The civil works under the program will be relatively small and will be widely distributed throughout Naryn Region.
5. The Program Safeguards Officer has prepared a list of key documents on Program's Social Safeguards as of 31 December 2025 (see Annex 2).

2 PROGRAM DESCRIPTION AND CURRENT ACTIVITIES

2.1 Program Description

6. The proposed Asian Development Bank (ADB) assistance contributes to the Government of the Kyrgyz Republic's national development strategy, 2018–2040, goal of clean water and sanitation for all. The government's state (nationwide) program for the water and sanitation sector, the Strategy for the Development of Water Supply and Sewerage Systems in Settlements of the Kyrgyz Republic, 2016–2026, is aimed to improve access to safe and quality water supply and sanitation (WSS) services in all settlements. The government program sets out the strategic and policy framework to develop WSS infrastructure and services, and improve the capacity of government departments, agencies, and operators for the sustainable delivery of WSS services. The focus of ADB's operation is a results-based approach to support the government program to achieve inclusive and reliable access to safe water supply and improved sanitation for rural communities.
7. The government program in expanding access to safe water supply and improved sanitation for rural communities in Naryn Region, as requested by the government. The Program will therefore support infrastructure construction and rehabilitation, backed up by measures to strengthen the capacity of the Community Development and Investment Agency (ARIS), the implementing agency, operators, and improve the sustainable management of the WSS facilities.
8. ARIS was established by a Decree of the President of the Kyrgyz Republic dated 15 October 2003 in order to deepen measures taken to attract investments to overcome poverty, develop and support private entrepreneurship within the framework of the National Poverty Reduction Strategy, strengthen the activities of local governments and strengthening local communities and community organizations. ARIS is a nonprofit organization with the status of a legal entity.
9. The results-based lending (RBL) modality is the most suitable for this program since:
 - (i) there is a clearly defined scope for development partners' support;
 - (ii) given ADB's prior involvement in rural WSS, the RBL modality provides the opportunity for all stakeholders to work together and demonstrate strong commitment to achieving verifiable results;
 - (iii) the modality is able to incentivize institutional strengthening in procurement, internal audit function, and sustainable operations and maintenance of WSS facilities at the community level;

- (iv) the strengthened mechanisms will pave the way for future stepped-up engagement in the sector; and
 - (v) the RBL modality will sharply reduce transaction costs, given the multiple small transactions at village and district level required by the Program.
10. At the impact level, the RBL program is aligned with the government's goal of improving the health and quality of life of residents and reducing adverse environmental impact by 2026. The program's outcome will be inclusive and reliable access to safe water supply and improved sanitation for rural communities in Naryn Province. Due to the limited availability of funds, the priority focus will be on 64,000 population. Two output level results will contribute to the outcome:
- Output 1: water supply and sanitation infrastructure expanded and sanitation solutions piloted, and
 - Output 2: institutional capacities strengthened for enhanced sustainability in the rural water supply and sanitation sector.
11. The ongoing RBL program aims to provide drinking water and sanitation to 64,000 rural people and support 21 educational and health institutions in Naryn Region.

Additional funding for Naryn Rural Water Supply and Sanitation Development Program. The additional financing will expand the existing scope of the current RBL program to cover 100,000 people and 37 educational and medical institutions, and will also support sector reform and climate change initiatives using the same funding modality. Additional financing for the Program includes 23 villages. More details are in Table 2.

Table 2: List of villages of Additional Financing of the Program

No.	Name of the District	Name of the Aiyl Okmotu ¹	Name of the Villages	Population (Data from Design Institute and National Statistics Committee of Kyrgyz Republic for 2022)
1	At-Bashy	At-Bashy	At-Bashy	20,150
2			Ak-Zhar	
3	Zhumgal	Min-Kush	Ken-Suu	534
4			Kotur-Suu	
5			Tabylgy	
6			Sary-Bulun	304
7			Kyzyl-Sook	217
8	Naryn	Zherge-Tal	Zherge-Tal	3,364
9		Min-Bulak	Ornok	637
10			Echki-Bashy	1,979
11		Dobolu	Ottuk	1,771
12			Kenesh	752
13			Alysh	544
14			Emgek-Talaa	Emgek-Talaa
15		Chet-Nura	Ak-Bulun	325
16	Kochkor	Kum-Dobo	Arsy	769
17		Ormon-Han	Semiz-Bel	1,327
18			Epkin	1,890
19			Tendik	4,643
20		Cholpon	Tuz	1,560
21		Kara-Suu	Kyzyl-Dobo	2,068
22	Ak-Talaa	Kara-Burgon	Zhany-Tilek	376
23		Baetov	Ugut	917
Total			23	46,088

The Loan and Grant Agreements for the Program additional financing between the Cabinet of Ministers of the Kyrgyz Republic and the ADB were signed on 4 November 2024 in Bishkek city.

The Law of the Kyrgyz Republic No. 83 dated 28 April 2025 "On Ratification of the Loan Agreement between the Kyrgyz Republic and the Asian Development Bank for the project "Naryn Rural Water Supply and Sanitation Development Program - Additional Financing" and the Grant Agreement between the Kyrgyz Republic and the Asian Development Bank for the project "Naryn Rural Water Supply and Sanitation Development Program - Additional Financing" signed on 4 November 2024 in Bishkek City" was adopted.

¹ Aiyl Okmotu (village board) – is the executive-administrative body of the aiyl (village) or village council managing within the limits of his authority, the affairs of life support and the life activities of the local community.

2.2 Program Contacts and Management

12. The Program will be executed under the overall responsibility of Department of “Drinking Water Supply and Sewerage Development” (DDWSSD), under the Ministry of Water Resources, Agriculture and Processing Industry of the Kyrgyz Republic. The Program implementation is carried out by ARIS. ARIS works in close cooperation with the DDWSSD, participating Aiyl Okmotus (AOs) and other key the Program stakeholders and counterparts (see Table 3).

Table 3: Responsibility of Partner Organizations in the Program Implementation

No.	Organization	Responsibilities
1	Asian Development Bank PTL Yuto Hyakukan yhyakukan@adb.org Sophio Omanadze Safeguards Specialist (Social), ADB OSFG somanadze@adb.org Nargiza Kudaiberdieva Social Safeguards Officer Office of Safeguards (OSFG) Kyrgyz Republic Resident Mission ADB nkudaiberdieva@adb.org Chyngyz Sydykov National Resettlement Consultant, ADB KYRM csydykov.consultant@adb.org	ADB is the financing institutions that provides support for design and implementation of the Results-Based Lending (RBL) Program.
2	Executing Agency - SI DWSS Azamat Shadmanov Director enesay24.info@yandex.ru	This Department of “Drinking Water Supply and Sewerage Development” (DDWSSD) under the Ministry of Water Resources, Agriculture and Processing Industry of the Kyrgyz Republic is responsible for development of both the rural and urban water supply and sanitation sectors, including policy, planning and sector coordination. The DDWSS role in the program is as the overall executing agency, which includes, among other activities: overall sector coordination and policy support. Government and donor liaison, participation in all procurement activities (for example, as a member of evaluation committee), identification and prioritization of sector interventions (including infrastructure investments and institutional support), and as the responsible agency of the cabinet of Ministers of the Kyrgyz Republic, provision of support to ARIS in implementation (as required)
3	Program Implementing agency - ARIS Ulan Baigonchokov – The Program Coordinator UBaigonchokov@aris.kg Beknazar Abduraimov – The Program Safeguards Officer BAbduraimov@aris.kg Kanybek Jumaliev- Consultant/Social Safeguards Specialist kanybek.jumaliev@mail.ru	ARIS will be responsible for overall program implementation, including fiduciary and safeguards compliance. ARIS was created by Decree of the President of the Kyrgyz Republic in October 2003 as a legally and operationally autonomous institution

No.	Organization	Responsibilities
4	Heads of Naryn District State Administration - Akims	Executive power in the region is carried out by the local state administration. The local state administration is a state executive body that ensures the coordinated activities of territorial divisions of ministries, state committees, administrative departments, and other state bodies of the Kyrgyz Republic within the territory of the districts, their interaction with local governments and exercising state control over their activities in terms of functions and powers delegated
5	"Kyrgyzgiprostroy» OJSC Design Institute Andrey Putilov Chief Design Engineer gipro75@mail.ru Olga Zinina, Environmental Specialist zinola@yandex.com Yuri Dolgov - Resettlement Consultant. a_doc@mail.ru	The design institute is responsible for development of detailed design and cost estimation documentation (DED) for 13 villages in the Naryn Region (Stage I): <ul style="list-style-type: none"> - Tosh-Bulak, Oruk-Tam, Orto-Saz, Ak-Kiya, Zhalgyz-Terek, Zherge-Tal, Zhan-Bulak, Kulanak, Uchkun Villages in Naryn district; - Baetov and Kaiyndy-Bulak Villages in Ak-Tala district; - At-Bashi and Ak-Zhar Villages in At-Bashyn district.
6	"ENKON" LLC Design Institute Alexander Khromov encon@mail.ru Olga Zinina, Environmental Specialist zinola@yandex.com Yuri Dolgov - Resettlement Consultant. a_doc@mail.ru	The design institute is responsible for development of detailed design and cost estimation documentation (DED) for 15 villages in the Naryn Region (Stage II): <ul style="list-style-type: none"> - Zherge-Tal Village in Ak-Tala district; - Kyzyl-Sook, Sary-Bulun, Ken-Suu, Kotur-Suu, Tabylyg, Aral, Kichi-Aral, Lama, Chaek, Besh-Terek Villages in Zhumgal district; - Moldo-Kylych, Isakeyeva, Kochkor, Kara-Too Villages in Kochkor district
7	Consortium LLC Design Institute "ENKON" and OJSC Design Institute "KyrgyzGiprostroy" Khromov Alexander Sergeevich encon@mail.ru Andrei Alekseevitch Putilov, Chief Design Engineer Gipro75@mail.ru Environmental Specialist Zinina Olga Valerievna	The design institutes are responsible for development of detailed design and cost estimation documentation (DED) for 15 villages in the Naryn Region (Stage III): <ul style="list-style-type: none"> - Arsy, Semiz-Bel, Tuz, Epkin, Kyzyl-Dobo and Tendik Villages in Kochkor district; - Ornok, Kenesh, Alysh, Emgek-Talaa, Echki-Bashy, Ottuk and Ak-Bulun Villages in Naryn district; - Zhany-Tilek and Ugut Villages in Ak-Tala district.
8	Construction Contractors: Consortium LLC "EKARAS-5" and LLC "Construction company "Sher-Kurulush" ekaras777@mail.ru OJSC "YUG-STROYSERVIS" almazbekKD-77@mail.ru LLC "Metag Inshaat Tijaret Anonym Shirketi" metagkg@gmail.com LLC "MS Building" CJSC "Kaynar" zaokaynar@mail.ru Consortium "Profit-Express" LLC and "Turan Grupp" LLC profit-express@mail.ru	Responsible for the construction of water supply systems in compliance with the requirements of the site-specific environmental management plan and occupational health, safety and environment

13. Active contracts within the framework of the Program are shown in Table 4.

Table 4: Program Contracts

No.	Name of the Village	Contracts, Dates	Title	Construction Contractors
1	Zherge-Tal in Ak-Talaa District	ARIS-ADB-NRWSSDP-CW-NCB-DLI-1-04, 30.06.2023	Construction of a water supply system for the Zherge-Tal subproject	"YUG- STROYSERVIS" OJSC
2	Ak-Kiya	ARIS-ADB-NRWSSDP-CW-NCB-DLI-1-03, 07.07.2023	Construction of a water supply system in villages of Chet-Nura aiyl aimak (subproject Ak-Kiya)	Consortium: "EKARAS-5" LLC and "Construction company "Sher- Kurulush" LLC
3	Lama, Aral, Kichi-Aral, Besh-Terek, Chaek (zone #4)	ARIS-ADB-NRWSSDP-CW-NCB-DLI-1-06/RT/L1, 21 June 2024	Construction of WSS in Lama, Aral, Kichi-Aral, Besh-Terek and Chaek Villages (Lot #1)	"Metag Inshaat Tijaret Anonym Shirketi" LLC
4	Chaek (zones #1, #2, #3)	ARIS-ADB-NRWSSDP-CW-NCB-DLI-1-06/RT/L2, 21 June 2024	Construction of WSS in the Chaek Village (Lot #2)	"Metag Inshaat Tijaret Anonym Shirketi" LLC
5	Kochkor	ARIS-ADB-NRWSSDP-CW-NCB-DLI-1-07/RT/L1, 21 June 2024	Construction of a water supply systems in the Kochkor Village (Lot #2)	"Metag Inshaat Tijaret Anonym Shirketi" LLC
6	Kara-Too, Isakeev, Moldo-Kylych	ARIS-ADB-NRWSSDP-CW-NCB-DLI-1-07/RT/L2, 21 June 2024	Construction of a water supply systems in Kara-Too, Isakeev, Moldo-Kylych Villages (Lot #1)	"Metag Inshaat Tijaret Anonym Shirketi" LLC
7	Baetovo	ARIS-ADB-NRWSSDP-CW-NCB-DLI-1-08/L1, 21 June 2024	Construction of WSS in the Baetov AO (Baetovo Village, Lot#1)	"MS Building" LLC
8		ARIS-ADB-NRWSSDP-CW-NCB-DLI-1-08/L2, 21 June 2024	Construction of WSS in the Baetov AO (Baetov Village, Lot #2)	"Metag Inshaat Tijaret Anonym Shirketi" LLC
9	Kaindy-Bulak	ARIS-ADB-NRWSSDP-CW-NCB-DLI-1-08/L3, 21 June 2024	Construction of WSS in the Baetov AO (Kaiyndy-Bulak Village, Lot #3)	"Metag Inshaat Tijaret Anonym Shirketi" LLC
10	Uchkun	ARIS-ADB-NRWSSDP-CW-NCB-DLI-1-09/L1, 14 February 2025	Construction of WSS in Uchkun and Kok-Zhar Villages (Lot #1)	Consortium "Profit-Express" LLC and "Turan Grupp" LLC
11	Kulanak	ARIS-ADB-NRWSSDP-CW-NCB-DLI-1-09/L2, 14 February 2025	Construction of WSS in Kulanak Village (Lot #2)	
12	Zherge-Tal in Naryn District	ARIS-ADB-NRWSSDP-AF-CW-NCB-DLI-1-10, 11 March 2025	Construction of WSS in Zherge-Tal Village	CJSC "Kaynar"

14. Implementation of the Program has been started in all districts of Naryn Region therefore ARIS is cooperating with the Aiyl Okmotu Heads. The table below is a list of Aiyl Okmotus established after administrative and territorial reform in accordance with a Decree of the President of the Kyrgyz Republic # 85 dated 3 April 2023² (see Table 5).

Table 5: Contact Details of Local Self-Government Bodies covered by the Program

No.	Name of Aiyl Okmotu	Aiyl Okmotu Head	Contact Phone	Website, Email Address
1	Chet-Nura AO	Turatbek Kuleshov	(03522) 6-00-21	chetnura.naryn-region.kg
2	Zherge-Tal AO in Naryn District	Talantbek Sydykbekov	(03522) 5-14-25	jergetal.naryn-region.kg
3	Zhan-Bulak AO	Kubanychbek Toktoraliyev	(03522) 6-09-13	janbulak.naryn-region.kg
4	Uchkun AO	Almasbek Botoiarov	(03522) 3-63-28	uchkun.naryn-region.kg uchkun.okmot@mail.ru
5	Baetov AO	Arstanbek Akiev	(03537) 9-15-12	baetov.naryn-region.kg
6	Ala-Buga AO in Ak-Talaa District	Ulukbek Nuraliev	(03537) 6-07-43	zhergetal-ao@mail.ru
7	At-Bashi AO	Ruslan Dokoev	(03534) 2-31-66	atbashyao@inbox.ru
8	Min-Kush AO	Ilgiz Ernis uulu	(03536) 3-12-81	
9	Zhumgal AO	Atilla Tugolbekov	(03536) 2-27-26	jumgal.naryn-region.kg
10	Chaek AO	Taalibek Kuchmuratov	(03536) 2-37-13	chaekaiylokmotu@mail.ru
11	Cholpon AO	Zakir Kozubekov	(03535) 2-25-57	
12	Ormon-Han AO	Talant Abdylidaev	(03535) 2-15-33	niazbekovna@mail.ru
13	Kum-Dobo AO	Mirlan Israilov	(03535) 2-19-56	schorgoeva@gmail.com

15. Based on the tender results on selection of a consultant to develop detailed design and cost estimation documentation (DED) for rural water supply infrastructure in the Naryn Region, the following contracts were signed:

A. With the KYRGYZGIPROSTROY OJSC Design Institute, the first contract No. ARIS-ADB-NRWSSDP-QCBS-01-2021 dated 15 September 2021. Table below is reflecting the list of villages for which, the DED packages were developed under this Contract (see Table 6).

² <https://cbd.miniust.gov.kg/5-10087/edition/1272313/ru>

Table 6: Information on the Program Subprojects under the First Contract for DED Packages (KYRGYZGIPROSTROY OJSC Design Institute)

No.	Name of the District	Name of the Aiyl Okmotu	Name of the Subproject	Village Covered under the Subproject	Population	
1	Naryn	Chet-Nura	Tosh-Bulak	Tosh-Bulak	210	
2			Oruk-Tam	Oruk-Tam	197	
3			Orto-Saz	Orto-Saz	820	
No.	Name of the District	Name of the Aiyl Okmotu	Name of the Subproject	Village Covered under the Subproject	Population	
4	Ak-Talaa	Baetov	Ak-Kyia	Ak-Kyia	985	
5			Zherge-Tal	Zhalgyz-Terek	Zhalgyz-Terek	1,245
6				Zherge-Tal	Zherge-Tal	3,364
7			Zhan-Bulak	Zhan-Bulak	Zhan-Bulak	2,527
8			Uchkun	Kulanak	Kulanak	6,544
9					Uchkun	
10			Baetov	Baetov	Baetov	11,893
11				Kaiyndy-Bulak		
12			At-Bashy	At-Bashy	At-Bashy	20,150
13	Ak-Zhar	Ak-Zhar				
TOTAL	3	7	10	13	47,935	

B. With the ENKON LLC Design Institute, the second contract No. ARIS-ADB-NRWSSDP-QCBS-02-2021 dated 16 November 2021.

Table below is reflecting the list of villages for which, the DED packages were developed under this Contract (see Table 7).

Table 7: Information on the Program Subprojects under the Second Contract for DED Packages (ENKON LLC Design Institute)

No.	Name of the District	Name of the AO	Name of the Subproject	Village Covered under the Subproject	Population
1	Ak-Talaa	Ala-Buga	Zherge-Tal	Zherge-Tal	585
2	Zhumgal	Min-Kush	Kyzyl-Sook	Kyzyl-Sook	217
3			Sary-Bulun	Sary-Bulun	304
4			Kabak	Ken-Suu	534
5				Kotur-Suu	
6				Tabylgy	
7			Chaek	Chaek	13,535
8		Беш-Теpek			
9		Aral		Aral	660
10				Kichi-Aral	
11		Zhumgal	Lama	Lama	636
12		Kochkor	Cholpon	Moldo-Kylych	Moldo-Kylych
13		Ormon-Han	Isakeyev	Isakeyev	2,287
14			Kochkor	Kochkor	14,397
15		Kum-Dobo		Kara-Too	
TOTAL	3	7	10	15	34,245

C. With the ENKON LLC Design Institute and Kyrgyzgiprostroy OJSC Design Institute, the third contract No. ARIS-ADB-NRWSSDP-CS-QCBS-2023-1 dated 15 July 2023.

Table below is reflecting the list of villages for which, the DED packages are being developed under this Contract (see Table 8).

Table 8: Information on the Program Subprojects under the Third Contract for DED Packages (Consortium ENKON LLC and Kyrgyzgiprostroy OJSC)

No.	Name of the District	Name of the AO	Name of the Subproject	Village Covered under the Subproject	Population	DED readiness status
1	Kochkor	Kum-Dobo	Arsy	Arsy	762	ready
2		Ormon-Han	Semiz-Bel	Semiz-Bel	1,476	ready
3			Tendik	Tendik	4,716	ready
4		Cholpon	Tuz	Tuz	1,458	under development
5			Epkin	Epkin	1,651	ready
6		Kara-Suu	Kyzyl-Dobo	Kyzyl-Dobo	2,174	ready
7	Naryn	Min-Bulak	Ornok	Ornok	629	under development
8			Echki-Bashy	Echki-Bashy	1,912	under development
9			Ottuk	Ottuk	1,741	under development
10		Dobolu	Kenesh	Kenesh	719	under development
11			Alysh	Alysh	539	under development
12		Emgek-Talaa	Emgek-Talaa	Emgek-Talaa	1,961	under development
13		Chet-Nura	Ak-Bulun	Ak-Bulun	343	under development
14	Ak-Tala	Kara-Burgon	Zhany-Tilek	Zhany-Tilek	622	under development
15		Baetov	Ugut	Ugut	1,058	under development
Total	3	11	15	15	21,761	-

2.3 The Program Activities During the Current Reporting Period

16. **Subprojects completed in 2023-2025:** Orto-Saz, Zhalgyz-Terek, Zhan-Bulak, Tosh-Bulak, Oruk-Tam and Ak-Kiya in Naryn District.

Zherge-Tal in Ak- Tala District.

Active subprojects:

Lama, Aral (Aral and Kichi-Aral villages), Chaek (Chaek and Besh-Terek villages) in Zhungal District;

Kochkor (Kochkor and Kara-Too villages), Isakeev, Moldo-Kylych in Kochkor District;

Baetov (Baetovo and Kaiyndy-Bulak villages) in Ak-Tala District;

Kulanak (Kulanak and Uchkun villages), Zherge-Tal in Naryn District.

Water supply sources in villages:

- 1) Orto-Saz Village - borehole;
- 2) Zhalgyz-Terek Village - borehole;
- 3) Zhan-Bulak Village - borehole;
- 4) Tosh-Bulak Village - spring capture;
- 5) Oruk-Tam Village - spring capture;
- 6) Ak-Kiya Village - borehole;
- 7) Zherge-Tal Village (in Ak-Tala District) - spring capture;
- 8) Lama Village - spring capture;
- 9) Aral Village - borehole;
- 10) Kichi-Aral Village - borehole;
- 11) Besh-Terek Village - spring capture;
- 12) Chaek Village - spring capture;
- 13) Kochkor Village - borehole;
- 14) Kara-Too Village - borehole;
- 15) Isakeev Village - borehole;
- 16) Moldo-Kylych Village - borehole;
- 17) Baetov Village - borehole;

- 18) Kaiyndy-Bulak Village - borehole;
- 19) Kulanak Village - spring capture;
- 20) Uchkun Village - borehole;
- 21) Zherge-Tal Village (in Naryn District) - spring capture;
- 22) At-Bashy Village - underflow waters (drainage in the form of tapping);
- 23) Ak-Zhar Village - underflow waters (drainage in the form of tapping);
- 24) Kyzyl-Sook Village - underflow waters (drainage in the form of tapping);
- 25) Sary-Bulun Village - spring capture;
- 26) Ken-Suu Village - spring capture;
- 27) Kotur-Suu Village - spring capture;
- 28) Tabylgy Village - spring capture.

17. The following construction and installation works (CIW) were completed during the reporting period (see Table 9).

Table 9: Brief Information on Construction Work Contracts and Status

No.	Villages	Contractors	Contract Signing Date	Civil Works		Completed Works	Overall Progress as of 31 December 2025
				Start Date	End Date		
1	Zherge-Tal in Ak-Talaa District	"YUG- STROYSERVIS" OJSC	30 June 2023	30 June 2023	30 December 2024	The water intake area and reservoir site are completely fenced. All water intake and reservoir facilities have been built. The water supply and village networks have been completed, etc.	100 %
2	Ak-Kyia	Consortium LLC "EKARAS-5" and Sher-Kurulush LLC»	7 June 2023	7 June 2023	30 June 2025	The water intake area is completely fenced. All water intake and reservoir facilities have been built. The water supply and village networks have been completed, etc.	100 %
3	Lama	Metag Inshaat Tijaret Anonym Shirketi LLC Lots #1	21 June 2024	21 June 2024	30 June 2026	Installation of transformer -1 set. Construction of strip foundation for guardhouse and chlorination room. Construction of fencing for the reservoir site. Construction of 2-kilometer road to catchment. Laying down PE pipes: d=110 mm - 1,903 m; d=90 mm - 2,826 m; d=63 mm-2,322 m; Installation of reinforced concrete wells - 65 pcs. Construction and installation works are ongoing.	90 %
4	Aral and Kichi-Aral					Laying PE pipes: d=90 mm - 5,844 m, d=75 mm - 397 m, d=63 mm - 4,124 m. Installation of reinforced concrete wells - 70 pcs. The tank's sub-concrete has been poured. The foundation for the chlorination room and the guardhouse has been poured. A Complete transformer substation (CTS) - 6/0.4 kV - 25 kVA has been installed and construction of fencing for the water intake site.	78 %
5	Besh-Terek					Laying of the PE pipes for village network - 8,564.2 m. Laying of the water main from PE pipes - 1,780 m. Installation of reinforced concrete wells - 59 pcs. Catchment chambers are completed by 70% of the total volume. The guardhouse and chlorination plant buildings have been constructed, and the fence has been erected. The foundation for the guardhouse has been poured the reservoir is under construction.	90 %

No.	Villages	Contractors	Contract Signing Date	Civil Works		Completed Works	Overall Progress as of 31 December 2024
				Start Date	End Date		
6	Chaek zone #4)					Installation of a water pipeline made of PE pipes: d=160 mm – 1,354 m, d=225 mm – 762 m. Installation of reinforced concrete wells - 589 pcs. Also, works are carried out to rehabilitate sanitary facilities in the building of the kindergarten.	70 %
7	Chaek(Zones #1, #2, #3)	Metag Inshaat Tijaret Anonym Shirketi LLC Lots #2	21 June 2024	21 June 2024	30 June 2026	Construction of the reservoir (concrete works are in progress). PE pipes laid: d=225 mm – 17,168.00 m, d=160 mm – 20,915.50 m, d=110 mm – 6,453.10 m, d=63 mm – 6,612.10 m. Construction and installation works are ongoing. The reservoir has been constructed (concrete work is underway).	70 %
8	Kochkor	Metag Inshaat Tijaret Anonym Shirketi LLC Lots #2	21 June 2024	21 June 2024	30 June 2026	Installation of a water pipeline made of PE pipes: d=250 mm – 1,000 m, d=225 mm – 1,249 m, d=160 mm – 1,811 m, d=110 mm – 2,578 m, d=90 mm – 1,607 m, d=63 mm – 4,663 m. A new borehole was drilled. Rehabilitation of the existing borehole has been carried out. Installation of reinforced concrete wells - 170 pcs. The installation of the water tower has been completed. Construction and installation work is underway.	45 %
9	Kara-Too					A 70-m borehole has been drilled. Drilling operations were fully completed, and the well was plugged and abandoned. Laying of PE pipes: d=110 mm – 2,354.2 m, d=90 mm – 2,708.4 m, d=63 mm – 1,265.8 m. Installation of reinforced concrete wells - 68 pcs. The water supply networks were fully laid down. Construction and installation works are ongoing.	80 %
10	Isakeev	Metag Inshaat Tijaret Anonym Shirketi LLC Lots #1	21 June 2024	21 June 2024	30 June 2026	The sanitary facilities in the building of the Secondary School named after Satarkul Ismailov have been rehabilitated. Construction and installation works are ongoing. Laying PE pipes: d=110 mm – 2,900 m. Posts have been installed to fence off the water intake site.	85 %
11	Moldo-Kylych					PE pipes d=110 mm – 40 m were laid at the reservoir site. Reinforced concrete wells were installed - 31 pcs. A borehole with 80 m depth has been drilled. Drilling works were fully completed. Laying of PE pipes: d=110 mm – 2,061 m, d=63 mm – 1,712 m, d=90 mm – 1,630 m. The village roads and streets were restored after completion of excavation works. Construction and installation works are ongoing.	80 %

No.	Villages	Contractors	Contract Signing Date	Civil Works		Completed Works	Overall Progress as of 31 December 2024
				Start Date	End Date		
12	Baetov	“MS Building” LLC and «Metag Inshaat Tijaret Anonym Shirketi» LLC Lots #1 and #2	21 June 2024	21 June 2024	31 December 2025	Wells #1, #2, #3 and #4 have been drilled (with 80 m deep). Drilling works were fully completed. Laying of PE water supply pipes: d=160 mm - 800 m, d=180 mm - 800 m, d=250 mm - 400 m. Laying of PE network pipes: d=160 - 420 m, d=110 - 1,458 m, d=90 - 457 m. Installation of reinforced concrete wells - 22 pcs. The sanitary facilities in the building of the Secondary School named after Shukurbek Beishenaliev have been rehabilitated.	36 %
13	Kaiyndy-Bulak	Metag Inshaat Tijaret Anonym Shirketi LLC Lots # 2 and 3	21 June 2024	21 June 2024	31 December 2025	Drilling operations were completed. Laying of PE pipes: d=110 mm – 1,349 m, d=90 mm – 1,704.5 m. Installation of reinforced concrete wells - 22 pcs. Upon the completion of excavation works the village roads were restored.	85 %
14	Uchkun	Consortium “Profit-Express” LLC and “Turan Grupp” LLC Lots #1 and #2	14 February 2025	14 February 2025	30 August 2026	Laying the water pipeline from PE pipes: d=160 mm - 2,600 m. Construction and installation works are ongoing.	40 %
15	Kulanak					Laying the water pipeline from PE pipes: d=110 mm - 400 m. Construction and installation works are ongoing.	40 %
16	Zherge-Tal in Naryn District	“Kaynar” CJSC	11 March 2025	11 March 2025	11 September 2026	The following works on laying down the PE pipes were done: water main d=125 mm - 4,920 m and village network d=90 mm - 1,500 m. Installation of reinforced concrete wells -18 pcs. Construction and installation works are ongoing.	45 %

2.4 Description of Any Changes in the Program Design

18. Additional funding for the Rural Water Supply and Sanitation Development Program in the Naryn Region included 23 villages, where 46,088 people live.
19. The program safeguard systems assessment and the environmental assessment and review framework documents for additional financing for the Program have been updated and disclosed on ADB website

2.5 Description of Any Changes to Agreed Construction Methods

20. There were no changes to agreed construction methods.

3 SOCIAL SAFEGUARDS ACTIVITIES

3.1 General Description of Social Safeguards Activities

21. To ensure smooth program implementation, social safeguard monitoring shall be carried out by the program with the assistance by the technical supervision engineers to guarantee compliance with the social safeguards established for the program, including:
- monitoring the compliance with the ADB Safeguard Policy Statement requirements that no construction works can be started until the measures specified in the social safeguards due diligence report are implemented;
 - availability of a grievance redress mechanism (GRM), timely and effective review of grievances, if any, throughout the whole program implementation period;
 - observance by the contractor of ADB social safeguard requirements in accordance with the ADB Safeguard Policy Statement.
22. Throughout the program, the Program Safeguards Officer and the Social Safeguards Consultant/Specialist shall ensure regular supervision over functioning the grievance redress system under the program, and report any problems under the program, queries and complaints registered by affected persons, local authorities and other stakeholders.

3.2 Audit of the Sites

23. The Program Safeguards Officer has conducted the audit in terms of compliance with social safeguards measures in the subprojects, where construction and installation works have been carried out to construct the water supply systems (see Table 10).

Table 10: Site Visits and Audits

Organization	Performed by	Purpose	Summary of Significant Findings	Date
ARIS	Mr. Beknazar Abduraimov, Program Safeguards Officer	Monitoring and supervising the civil works in terms of compliance with health, safety and environment (HSE) requirements by the contractor at the sites of Lama Village	The contractor complied with all HSE. Workers have been provided with special clothing and personal protective equipment, etc.	5 July 2025, 12 August 2025, 18 September 2025, 21 October 2025
ARIS	Mr. Beknazar Abduraimov, Program Safeguards Officer	Monitoring and supervising the civil works in terms of compliance with HSE requirements by the contractor at the sites of Aral and Kichi-Aral Villages	The contractor complied with all HSE. Workers have been provided with special clothing and personal protective equipment, etc.	5 July 2025, 12 August 2025, 19 September 2025, 22 October 2025

Organization	Performed by	Purpose	Summary of Significant Findings	Date
ARIS	Mr. Beknazar Abduraimov, Program Safeguards Officer	Monitoring and supervising the civil works in terms of compliance with HSE requirements by the contractor at the sites of Chaek and Besh-Terek Villages	The contractor complied with all social safeguards.	5 July 2025, 12 August 2025, 19 September 2025, 22 October 2025
ARIS	Mr. Beknazar Abduraimov, Program Safeguards Officer	Monitoring and supervising the civil works in terms of compliance with HSE requirements by the contractor at the sites of Kochkor and Kara-Too Villages	The contractor complied with all social safeguards.	4 July 2025, 11 August 2025, 20 September 2025, 20 October 2025
ARIS	Mr. Beknazar Abduraimov, Program Safeguards Officer	Monitoring and supervising the civil works in terms of compliance with HSE requirements by the contractor at the sites of Isakeev and Moldo-Kylych Villages	The contractor complied with all social safeguards.	4 July 2025, 16 August 2025, 20 September 2025, 20 October 2025
ARIS	Mr. Beknazar Abduraimov, Program Safeguards Officer	Monitoring and supervising the civil works in terms of compliance with HSE requirements by the contractor at the sites of Baetovo and Kaindy-Bulak Villages	The contractor complied with all social safeguards.	2 July 2025, 13 August 2025, 15 September 2025, 23 October 2025
ARIS	Mr. Beknazar Abduraimov, Program Safeguards Officer	Monitoring and supervising the civil works in terms of compliance with HSE requirements by the contractor at the sites of Kulanak and Uchkun Villages	The contractor complied with all social safeguards.	3 July 2025, 14 August 2025, 17 September 2025, 25 October 2025
ARIS	Mr. Beknazar Abduraimov, Program Safeguards Officer	Monitoring and supervising the civil works in terms of compliance with HSE requirements by the contractor at the sites of Zherge-Tal Village	The contractor complied with all social safeguards.	3 July 2025, 14 August 2025, 17 September 2025, 25 October 2025

ADB and ARIS	Ms. Nargiza Kudaiberdieva, Social Safeguards Officer Office of Safeguards (OSFG) Kyrgyz Republic Resident Mission ADB; Mr. Lizandro Racoma, Safeguards Specialist (Environment), Office of Safeguards (OSFG) ADB and other representatives of the ADB Mission; Mr. Beknazar Abduraimov, Program Safeguards Officer	Review of key implementation mechanisms of the Original and Additional Financing for the Naryn Rural Water Supply and Sanitation Development Program.	ADB Mission representatives visited the Uchkun, Kulanak, Baetovo and Kaindy-Bulak Villages, where, in addition to construction and installation of the water supply system, they inspected the ongoing rehabilitation of sanitary facilities in the Uchkun Secondary School named after Toksobaev and in the Baetovo Secondary School named after Sh. Beishenaliev in. During the ADB Mission, Ms. Nargiza Kudaiberdieva, Social Safeguards Officer Office of Safeguards (OSFG) Kyrgyz Republic Resident Mission ADB and Mr. Lizandro Racoma, Safeguards Specialist (Environment), Office of Safeguards (OSFG) ADB, reviewed documents related to social and environmental safeguards.	8 October 2025
--------------	--	---	--	----------------

24. In all current subprojects, the civil works on construction of water supply systems have been carried out within the right-of-way zone and on Ayil Okmotu municipal lands.

25. There were no impacts on private assets such as fencing and vegetable gardens associated with construction within the subprojects.

Also, existing retail stores, pavilions and kiosks were not relocated.

26. **Results of auditing the sites.** Based on the inspection results in terms of compliance with social and environmental safeguards in subprojects, by the Program Safeguards Officer with the participation of the Technical Supervision Engineers and the contractor’s foremen, compiled Civil Work Monitoring and Supervision Checklists of construction works.

3.3 Tracking the Issues (based on Non-Conformance Notifications)

27. During the monitoring of the sites, no administrative requirements to eliminate the shortcomings of the occupational health, safety, and environmental protection (HSE) standards and requirements were issued.

3.4 Tendencies

28. There are some improvements by contractors of HSE aspects of working processes in this reporting period. Contractors comply with the construction schedule.

3.5 Unforeseen Social Impacts or Risks

29. During the reporting period and visual monitoring, the construction sites by the Program Safeguards Officer, no unforeseen impacts and risks on the social safeguards were identified during implementation of subprojects.

4 GRIEVANCE REDRESS MECHANISM AND BENEFICIARY FEEDBACK MECHANISM

4.1 GRM

30. The contractors' banners contain contact information of the ARIS Central Office, the ARIS beneficiary feedback mechanism (BFM), and contractor organizations for functioning the GRMs under the Program.
31. The GRM has been established in all villages of the Program: Lama, Aral, Kichi-Aral, Chaek, Besh-Terek, Kochkor, Kara-Too, Isakeev, Moldo-Kylych, Baetovo, Kaiyndy- Bulak, Kulanak, Uchkun and Zherge-Tal.
32. According to the provisions set out in the GRM, complaints and claims submitted during construction and installation works are reviewed by the Contractor.
33. There is a Logbook for community feedback and/or grievances in the foreman's field office of the Contractor.
34. As of 31 December 2025, no complaints were received from the local population. There were only positive comments from the local population in the Logbook for community feedback and/or grievances.
35. On October 8, 2025, during the ADB mission field trip to the Uchkun village, Uchkun Aiyl Aimak, Naryn District, Naryn Region, a village resident addressed with appeal. In his appeal, he noted that "the excavated trenches remained open, some pipes connected to houses were not properly installed, and the control over the works had not been was not monitored." This complaint was registered with the ARIS GRM.

On November 6th 2025, the complaint by village resident was reviewed in the Uchkun village, together with village resident and ARIS NRWSSDP Specialists (Infrastructure Engineer - Emil Ilyasov, BFM Specialist - Aziz Chalbaev, Technical Supervision Engineer - Nurlanbek Kudashov) and participation of the Contractor's representative - Site Manager Aibek Akynbekov.

At the meeting, the Claimant was briefed on the timeline and work scope of the "Kulanak" Subproject, which includes construction of a water supply system in the Uchkun village, as well as the construction requirements. Given that the Contractor's on-site workers are unable to answer all questions from village residents, it was suggested that residents contact the Site Manager directly with any further inquiries.

The Contractor's telephone number, as well as the BFM ARIS telephone number are displayed on banners posted at the sites where construction and installation works are being carried out.

The Program Specialists explained to the village resident all steps on implementation of civil works, promising to improve the control over civil works and quality of implementation. Following the explanations and clarifications, the Claimant accepted the above information and expressed satisfaction.

4.2 BFM

36. The ARIS BFM also functions, they are installed on notice boards of AOs, schools and kindergartens. The ARIS BFM main objective is the process of obtaining prompt and objective information and assessing and considering appeals (applications, proposals, complaints, requests, positive feedback) at all stages of Program implementation, which are received from citizens and/or beneficiaries to further improve their work.
37. Strengthen communication with Program beneficiaries and provide channels for feedback, as well as identify and resolve problems, increase transparency and accountability.
38. At all stages of implementation of ARIS projects, the Program stakeholders can submit requests on issues of their interest through the ARIS BFM information transfer channels.

ARIS BFM Channels:

- ✓ WhatsApp: + 996 (770) 70-05-22, Ph: + 996 (550) 70-05-22
 - ✓ ARIS website: www.aris.kg
 - ✓ ARIS online platform:
<https://kyrgyz-demo-republic-village-covid-19.yrpri.org/group/2831>
 - ✓ e-mail: bfm@aris.kg
 - ✓ Social networks: <https://www.facebook.com/kgariskg>
https://www.youtube.com/channel/UCRapQxzs_z6XEUIpAcc0_Q
 - ✓ Oral or written appeals
 - ✓ Letters delivered by hand
 - ✓ ARIS Reception: Bishkek, # 102, Bokonbaev Street
39. In its turn, ARIS will provide a response to each appeal in a timely and objective manner in accordance with the ARIS internal regulations and the legislation of the Kyrgyz Republic regulating the procedure for reviewing the citizens' appeals.

ANNEXES

Annex 1: Photos from the Construction Sites

Concreting around the well. Construction of a water pressure reducer (Lama Village, status: October 2025)



Construction of a reservoir. CTS (Aral village and Kichi-Aral village, status: August 2025)

Painting the fence around the tank site. Removing rust from the tank reinforcement (Besh-Terek village, status: September 2025)

Installation of shut-off valves. Construction of a reservoir (Chaek Village (zone #4), status: August 2025).



Earthworks. Rehabilitation of internal sanitary facilities in the kindergarten building (Chaek Village (zones 1, 2, and 3), status: September 2025)

Water tower site. Earthworks (Kochkor village, status: July 2025)

Water intake site. Contractor's concrete mixer trucks (Kara-Too Village, status: August 2025)



Earthworks. Posts for fencing off the reservoir site (Isakeev village, status: August 2025)



Earthworks. Reinforcement of the reservoir (Moldo-Kylch village, status: August 2025)

Sanitary facilities at the Secondary School. Fencing around the Secondary School septic tank (Baetovo Village, status: September 2025)




Testing of water pipes. Connection of private houses (Kayindy-Bulak Village, status: October 2025)

Earthworks. Installation of a well (Kulank and Uchkun Villages, status: October 2025)

Work on the reservoir site. Constructed water pressure reducer (Zherge-Tal village, status: August 2025)



ARIS BFM Banner (status: November 2025)

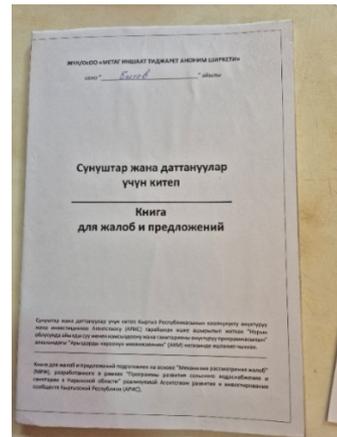

A Logbook for community feedback and/or grievances (Baetov Villages, Status in November 2025)



ADB Mission representatives also inspected construction of a water tower (Kaiyndy-Bulak Village, status: October 2025)



Review of documents relating to social and environmental safeguards (Uchkun Village, status: October 2025)



ADB Mission representatives met with ARIS (Bishkek, status: October 2025)

Annex 2: List of Key Documents on Program's Social Safeguards as of 31 December 2025

No.	Name of Document	Developed by	Approval Date
	Key Documents:		
1	Project Safeguards Systems Assessment. KGZ - 52256-001: Naryn Rural Water Supply and Sanitation Development Program	ADB, ARIS	June 2019 https://www.adb.org/sites/default/files/project-documents/52256/52256-001-pssa-en_1.pdf
	Reports:		
2	Semiannual social safeguards monitoring report for July-December 2023 under the program	ARIS	January 2024
3	Semiannual social safeguards monitoring report for January-June 2024 under the program	ARIS	July 2024
4	Semiannual social safeguards monitoring report for July-December 2024 under the program	ARIS	January 2025 https://www.adb.org/projects/documents/kgz-52256-001-
5	Semiannual social safeguards monitoring report for January-June 2025 under the program	ARIS	July 2025 https://www.adb.org/projects/documents/kgz-52256-001-
6	Semiannual social safeguards monitoring report for July-December 2025 under the program	ARIS	January 2026 https://www.adb.org/projects/documents/kgz-52256-001-smr-2
	Other Documents:		
